

TGP VIEWS ALL DOORS FROM THE SECURE SIDE

Please select the appropriate door handing configuration(s) as illustrated below.

LH	Left Hand Active	RH	Right Hand Active	LHR	Left Hand Reverse	RHR	Right Hand Reverse
LHA Pair	Left Hand Active & Right Hand Fixed Pair of Doors	RHA Pair	Right Hand Active & Left Hand Fixed Pair of Doors	LHRA Pair	Left Hand Reverse Active & Right Hand Reverse Fixed Pair of Doors		
RHRA Pair	Right Hand Reverse Active & Left Hand Reverse Fixed Pair of Doors	LHRA/RHRA Pair	Left Hand Reverse Active & Right Hand Reverse Pair of Doors	Double Egress	Dual Left Hand Reverse Pair of Doors		

Finish Floor Construction at Door Locations


At door locations, please specify the thickness from finish floor to subfloor to allow for proper installation and function of the factory installed automatic smoke seal. (See illustration below).

Material Type:
(check one)

- Carpet
- Tile
- Wood
- Other



Thickness: _____

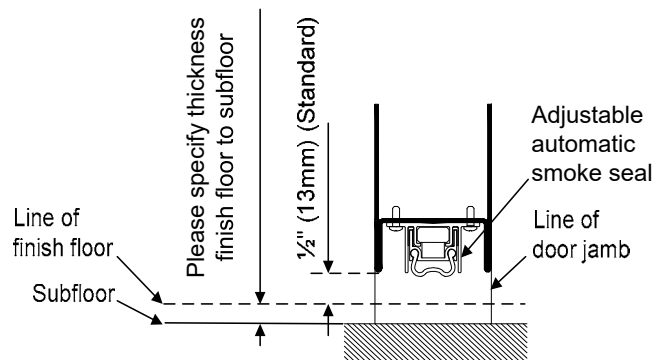

Door Leaf and Hardware by Others

TGP doors are supplied pre-hung with all hardware pre-installed and function tested. Upon request, TGP frames can be factory prepared to accept doors by others. In which case, hardware used on TGP doors must be reviewed for proper fit and functionality with our frame system. All manufacturer's templates, model numbers, layouts, locations, and in some cases, a physical sample of each hardware item must be received by TGP prior to fabrication. Manufacturing cannot begin until items have been approved by TGP for fabrication.
